


BCHS North Wing Renovation

WEEK OF July 13th, 2019

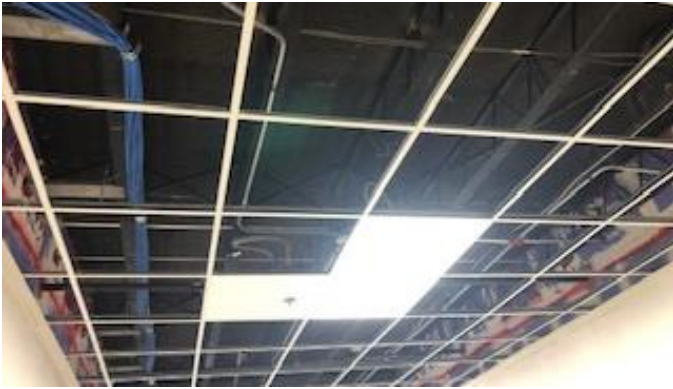

SAFETY

Safe Days Since Last Incident	32
Incidents to Date	0
First Aids to Date	0



WEATHER

Working Days	6
Days with Rain	0
Activities Delayed	0



SCHEDULE MILESTONES

- Hung and finished drywall in Group Toilets
- Completed tile in 1st and 2nd floor Group Toilets



MANPOWER

Number of Trades	6
Average Workers <i>(per day)</i>	28

TOP ACTIVITIES THIS WEEK

- Completed installing ceramic tile in 1st and 2nd floor group toilet areas.
- Hung drywall in group toilets
- Completed above ceiling cleanup in 1st floor commons area
- Installed ceiling grid in commons area
- Top and bottom portions of drywall painted in preparation for ceiling grid and ceramic tile base to be installed in group toilets.

UPCOMING ACTIVITIES

- Seal coat road by I2tech
- Install toilet fixtures in group toilet
- Hang markerboards and tack strips in classrooms
- Install ceiling grid in group toilet area
- Install sinks in group toilet area
- Paint commons area

