
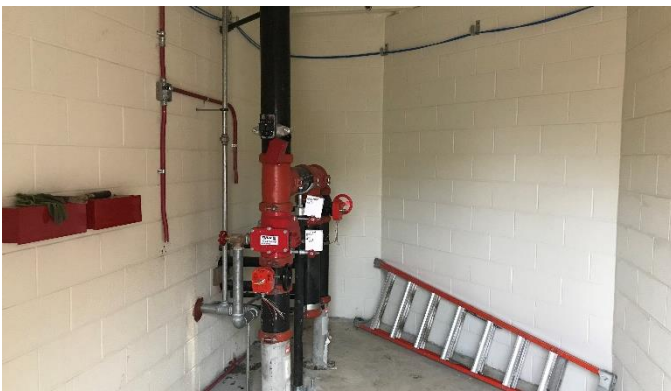


# BCHS Arena

WEEK OF Nov 09<sup>th</sup>, 2018

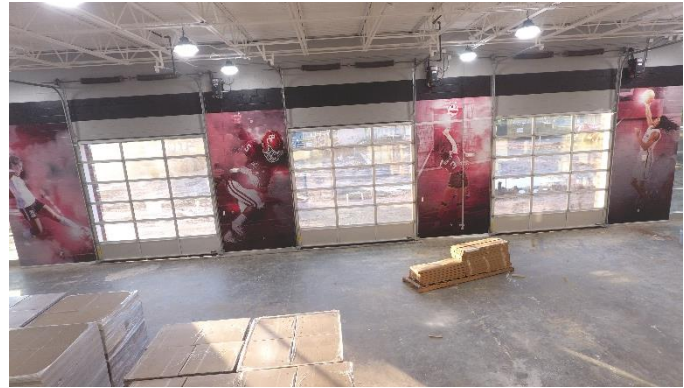

## SAFETY

Safe Days Since Last Incident	322
Incidents to Date	0
First Aids to Date	0



## WEATHER

Working Days	5
Days with Rain	5 (1.47")
Activities Delayed	6



## SCHEDULE MILESTONES

- Passed OSF overhead inspection



## MANPOWER

Number of Trades	16
Average Workers (per day)	13

### TOP ACTIVITIES THIS WEEK

- Scoreboards installed
- Basketball goals installed
- Sidewalk at NW corner installed
- Graphics installation began
- Polishing/staining of concrete floors completed (with exception of filming platforms)
- Stand alone trophy cases delivered
- Began terminations into F/A panel
- Arena speakers installed
- Ceiling tile delivered

### UPCOMING ACTIVITIES

- Begin sanding/sealing/painting of Arena floor
- Ceiling tile installation
- Washer/dryer delivery and installation
- Begin weight room turf and flooring installation
- Begin LVT installation
- Begin carpet installation

