


BCHS Arena

WEEK OF Nov 02nd, 2018

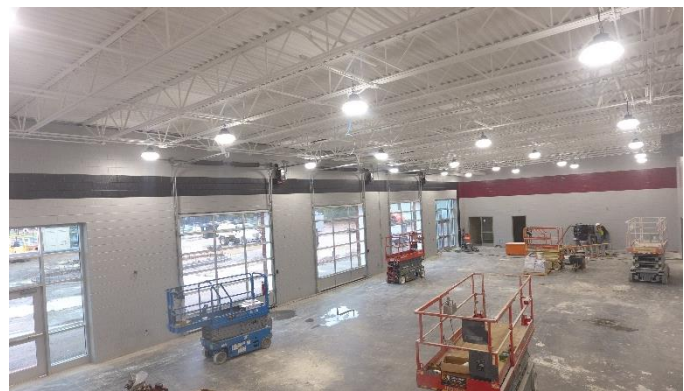

SAFETY

Safe Days Since Last Incident 315

Incidents to Date 0

First Aids to Date 0



WEATHER

Working Days 7

Days with Rain 1

Activities Delayed 3



SCHEDULE MILESTONES

- Interior paint completed



MANPOWER

Number of Trades 13

Average Workers (per day) 31

TOP ACTIVITIES THIS WEEK

- 3rd party overhead inspection completed and passed with 0 deficiencies
- Grade and begin curb installation at center of parking area
- Grade North side of site at Knox Abbott Drive
- Completed upper canopy fascia and soffits
- Toilet partition installation in area 3
- Walls painted and lights installed in weight room
- Entrance to lower parking area completed and parking lot being used for construction personnel

UPCOMING ACTIVITIES

- Scoreboard installation
- Practice goals installation
- Bleacher seat cushion install
- Begin exterior flatwork at North side of building (Knox Abbott)
- Begin ACM panel installation

