


# Riverbank Elementary

WEEK OF July 9<sup>th</sup>, 2018

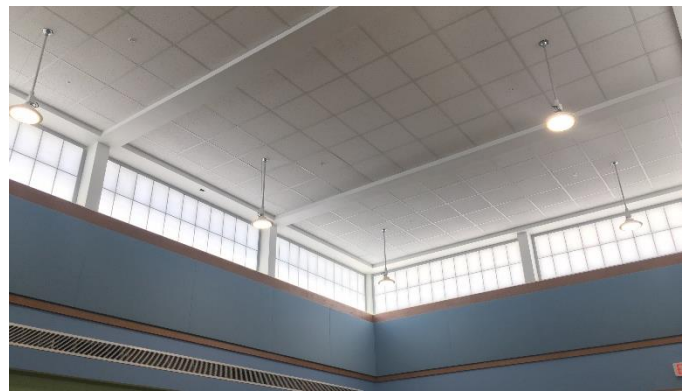

## SAFETY

Incidents to Date	2
First Aids to Date	1



## SCHEDULE

Current Completion August 1<sup>st</sup> 2018



## WEATHER

Working Days	6
Days of Weather Delay	0
Activities Delayed	0



## MANPOWER

Number of Trades	17
Average Workers <i>(per day)</i>	115

### TOP ACTIVITIES THIS WEEK

- Terrazzo Final Grind and Polish on 2<sup>nd</sup> Floor
- Asphalt, Crosswalk & Sidewalk prep/pour at Drop Off Loop
- Roller Shade Installation
- VRF Startup in Buildings C
- 2<sup>nd</sup> Floor Ceiling Tile
- Kitchen Equipment Startup Complete
- Irrigation Install ongoing
- Landscaping Behind Service Pad
- Acoustic Panels in Gym/Cafeteria
- Laminate Panels at Media Center
- Wood Doors and Hardware ongoing
- Secure Entry Curtainwall and Glazing
- Final Cleaning Buildings A, E & F

### UPCOMING ACTIVITIES

- Elevator Inspection Monday
- DHEC Kitchen Inspection Monday
- 3<sup>rd</sup> Party Pre-Final Re-Inspection Monday at 5:30
- OSF Final Wednesday the 18<sup>th</sup> at 8am
- Paving Bus Loop & Tie Ins
- Stage Curtain Installation
- VCT Waxing

