


Riverbank Elementary

WEEK OF June 25th, 2018

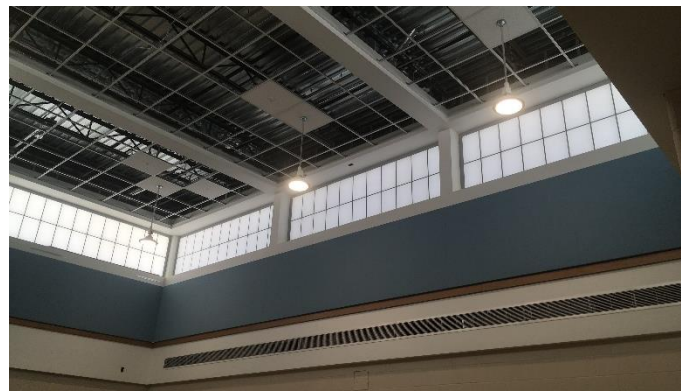

SAFETY

| | |
|--------------------|---|
| Incidents to Date | 2 |
| First Aids to Date | 1 |



SCHEDULE

Current Completion August 1st 2018



WEATHER

| | |
|-----------------------|---|
| Working Days | 6 |
| Days of Weather Delay | 4 |
| Activities Delayed | 3 |



MANPOWER

| | |
|-------------------------------------|-----|
| Number of Trades | 16 |
| Average Workers <i>(per day)</i> | 120 |

TOP ACTIVITIES THIS WEEK

- Sitework, Landscaping and Playground Turf delayed by heavy rains creating bad site conditions
- Second Floor OSF Overhead Inspection
- Terrazzo Final Grind and Polish in Main Lobby and 2nd Floor
- Curb/Stone Base & Sidewalk at Drop Off Loop
- Toilet Partitions/Bathroom Accessories in Buildings B, C & 2nd Floor
- VRF Startup in Buildings A & D
- MEP Connections to Kitchen Equipment
- Irrigation Install ongoing
- Landscaping at Pond
- Acoustic Panels in Clerestories
- Serving Line Storefront Glazing
- Ceiling Tile in Buildings A & D
- Playground Turf Installation

UPCOMING ACTIVITIES

- VRF Startup in Buildings B & C
- Ceiling Tile in Buildings B & C
- Kitchen Equipment Startup
- Wood Door Installation
- Elevator Inspection
- Terrazzo Grind and Polish in Cafeteria
- Paving Bus Loop & Tie Ins
- Secure Entry Curtainwall and Glazing

