



GALLAGHER

EST 1968

Construction Update – Thru August 24, 2018



Waxahachie ISD High School/Renovations

Construction Update thru August 24, 2018

ADMINISTRATION:

Waxahachie Independent High School – Bldg and Site Package
Contact: Clyde Melick

ARCHITECTS:

Corgan Architects
401 North Houston Street, Dallas, Texas 75202
214-263-0660
Contact: David Safir

CONSTRUCTION MANAGER:

Gallagher Construction Services
3501 Token Drive, Ste 100, Richardson, Texas 75082
972-633-0564
Contact: Lance Aaron

High School

Total Contract Sum	\$117,656,525
Total Completed To Date	\$105,145,142
Percent Complete	89%

High School Renovations

Total Contract Sum	\$2,996,682
Total Completed To Date	\$ 1,232,248
Percent Complete	41%

OVERALL PROJECT STATUS

Current Activities:

- Working on added scope: Fence at football field, added door at trash dumpster, and Finley benches
- Landscape and irrigation should be done in 2 weeks.
- Still waiting on bleachers to deliver at baseball field – Aug 24th

High School Renovation

- Area A completed and turned over to district.
- Tape, Bed and Paint ongoing at Areas B
- Start ceiling tile installation for Area B on Monday, August 27th
- Ceramic tile ongoing in Area B
- Started tape and bed of Area C

Waxahachie ISD High School Renovations

Construction Update thru August 24, 2018



Finishes started at Men's Restroom, Open office area in, and Hallway at main entry at Area B.

Waxahachie ISD High School Renovations

Construction Update thru August 24, 2018



Tape, bed and paint ongoing at Corridors, Main Conference Room and Reception Area at Area B

Waxahachie ISD High School Renovations


Construction Update thru August 24, 2018



CSG



Area A Cafeteria and
Main Corridor.

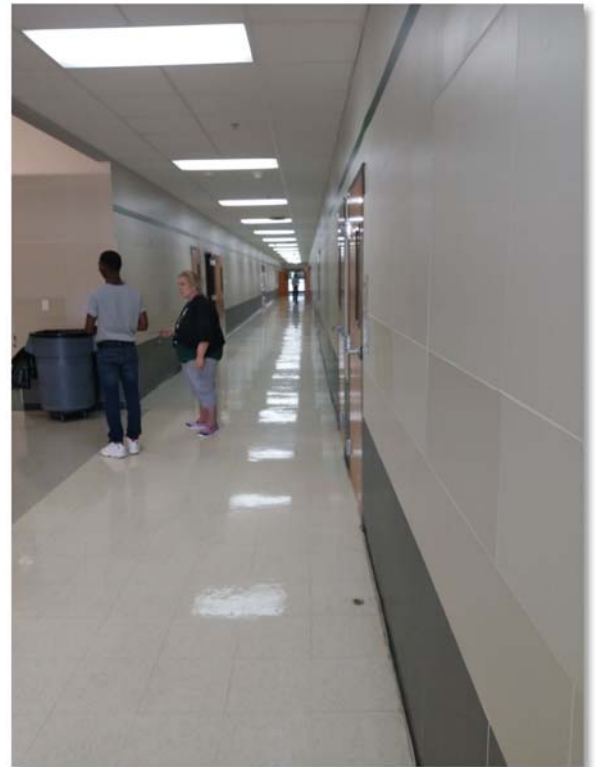

GALLAGHER CONSTRUCTION SERVICES
3501 TOKEN DR., SUITE 100, RICHARDSON, TX 75082
972.633.0564 • 972.633.0164 FAX
WWW.GALLAGHERTX.COM
