
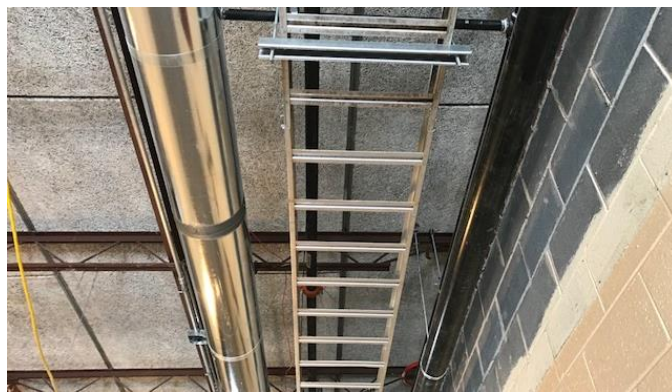
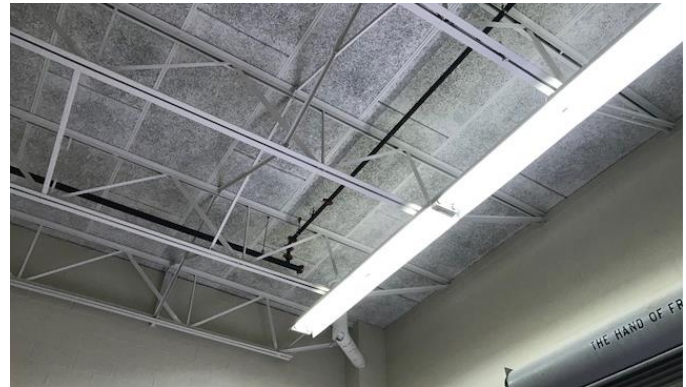


BCHS Renovation

WEEK OF October 19th, 2018



SAFETY

Safe Days Since Last Incident	103
Incidents to Date	0
First Aids to Date	1



WEATHER

Working Days	5
Days with Rain	0
Activities Delayed	0



SCHEDULE MILESTONES

- Completed in-wall testing at chase in group toilet
- Insulate piping in chase



MANPOWER

Number of Trades	6
Average Workers <i>(per day)</i>	31

TOP ACTIVITIES THIS WEEK

- In-wall plumbing testing passed at group toilets
- Hang duct in Corridor 103
- Installed sprinkler in Group Toilets, Fitness and Wellness, and Project Studio areas
- Completed framing in Project Studio
- Continued CMU walls in Group Toilets
- Start in-wall electrical rough-in Project Studio
- Continued sprinkler rough-in existing I2Tech areas

UPCOMING ACTIVITIES

- Continue overhead plumbing in group toilets
- Continue sprinkler rough in I2Tech
- Rough-in waste and vent piping in Backstage Area
- Remove HVAC unit above stage area
- Remove condensing unit from Auditorium area
- Demo HVAC unit over Project Studio and Group Toilet area
- Install beams for doors at Backstage areas

