



June 29, 2018

Belleville BOE  
Roof Replacement Projects  
Belleville High School  
ES School #3

Weekly Update: week ending 06/29/18

**Activities performed the week ending June 29, 2018**

- The contractor has mobilized at both Belleville HS and ES School #3 to commence roof replacement activities.
- The contractor has received and stored on site roofing materials for the HS as well as for ES School #3 roof replacement projects.
- The contractor has delivered and set up at both sites the hot tar kettles required for these roof replacement projects.
- Debris dumpsters have been delivered to both schools.
- The contractor has installed the required perimeter roof protection prior to commencing its roof replacement work.
- Roofing insulation has been craned to the roofs of both Belleville HS and ES School #3.
- Roof replacement activities have commenced simultaneously at both Belleville HS and ES School #3.
- The contractor is removing and replacing only that area of roofing that can be made watertight before the end of each work day.
- Daily housekeeping is being performed by the contractor at each project site to ensure the sites are maintained in a clean and safe manner.
- The ongoing work is monitored daily to ensure compliance with the project plans and specifications.

**Activities planned for the week commencing July 02, 2018**

- The contractor will continue roof replacement activities at both Belleville HS as well as ES School #3 as weather allows.

**Open Items**

- Upon completion of the roof replacement work at Belleville HS and ES School #3 the roofing contractor will immediately remobilize and commence roof replacement work at ES School #4 and ES School #10.

**Construction Progress Photos**



**June 2018: Belleville ES #3– Roofing materials being received on site.**




**June 2018: Belleville ES #3 –end of first day of roof replacement activities.**

**Construction Progress Photos (cont'd)**



**June 2018: Belleville HS – ongoing existing roof removals.**

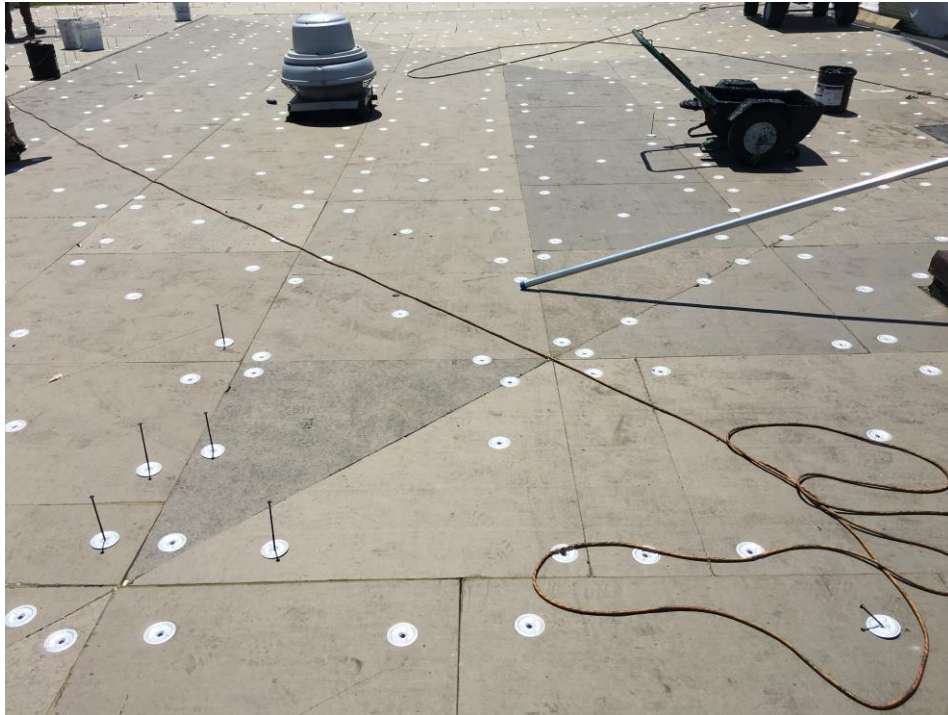

**June 2018: Belleville HS – new tapered insulation being installed over metal deck.**

**Construction Progress Photos (cont'd)**



**June 2018: Belleville HS –ongoing roof replacement day two.**



**June 2018: Belleville HS – kettle setup at the High School.**
