
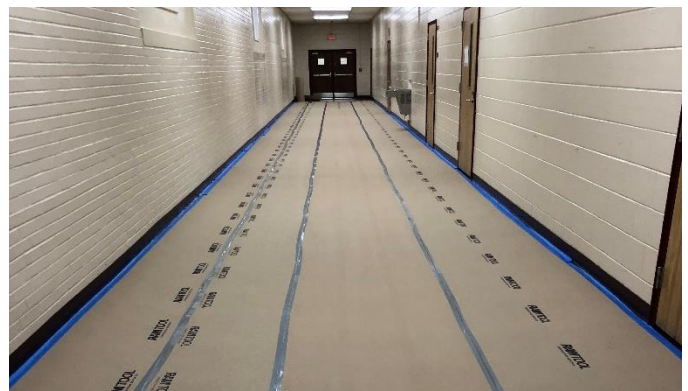


# BCHS Renovation

WEEK OF Feb 15th, 2019



## SAFETY

Safe Days Since Last Incident	192
Incidents to Date	0
First Aids to Date	2



## WEATHER

Working Days	5
Days with Rain	1
Activities Delayed	0



## SCHEDULE MILESTONES

- Sanded Auditorium Floor
- Received Certificate of Occupancy for Science and Technology



## MANPOWER

Number of Trades	5
Average Workers (per day)	20

### TOP ACTIVITIES THIS WEEK

- Continued installing proscenium in Auditorium
- Sanded Auditorium floor
- Patched damage wood flooring on stage
- Received Certificate of Occupancy for Science and Technology.
- Started up RTU in Fitness and Wellness
- Set thermostat in Fitness and Wellness
- Prepared second floor of Auditorium for demo work to start
- Plaster patching in Auditorium

### UPCOMING ACTIVITIES

- Cap Science and Technology roof
- Install main and branch sprinkler lines in Corridor A100.C
- Install casework in Backstage Area
- Install lighting at casework in Backstage Area
- Demo ceiling on second floor of Auditorium
- Start electrical clean up above ceiling on second floor of Auditorium

