


BCHS Renovation

WEEK OF October 13th, 2018

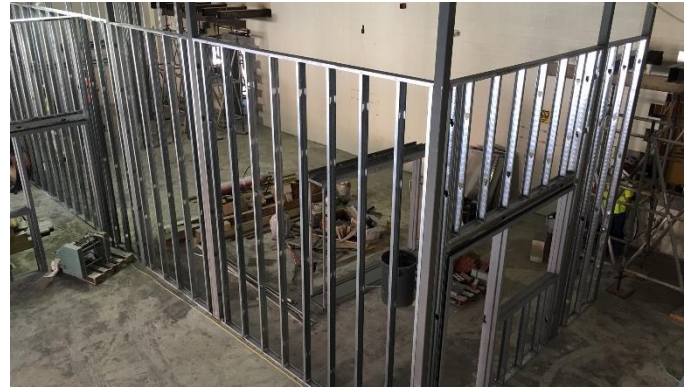

SAFETY

Safe Days Since Last Incident	98
Incidents to Date	0
First Aids to Date	1



WEATHER

Working Days	6
Days with Rain	2
Activities Delayed	0



SCHEDULE MILESTONES

- Installed Meter Pit
- Started CMU walls in Group Toilet
- Started sprinkler rough-in Science and Technology Building



MANPOWER

Number of Trades	7
Average Workers <i>(per day)</i>	29

TOP ACTIVITIES THIS WEEK

- Started framing in Project Studio
- Installed double bond beams for door openings in Project Studio
- Started electrical rough-in Auditorium
- Started sprinkler rough-in Project Studio and Group Toilet areas
- Started CMU wall in group toilets
- Installed Meter Pit
- Painted ductwork for Auditorium

UPCOMING ACTIVITIES

- Continue CMU walls in Group Toilets
- Hang duct in Group Toilet area
- Electrical In-wall rough-in Project Studio
- Continue Sprinkler rough-in existing I2Tech areas
- Remove HVAC unit above stage area
- Demo HVAC unit over Project Studio

