


# BCHS Arena

WEEK OF Nov 16<sup>th</sup>, 2018

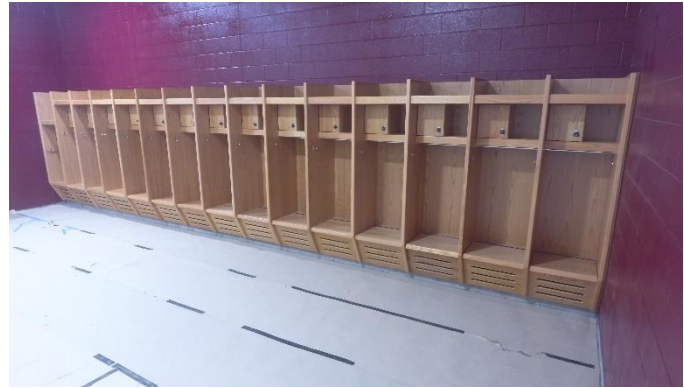

## SAFETY

Safe Days Since Last Incident	329
Incidents to Date	0
First Aids to Date	0



## WEATHER

Working Days	6
Days with Rain	4 (4.60")
Activities Delayed	6



## SCHEDULE MILESTONES

- Ceiling tile installed all areas



## MANPOWER

Number of Trades	15
Average Workers (per day)	10

### TOP ACTIVITIES THIS WEEK

- Arena floor sanded and sealed
- Began base cabinet installation
- Began solid surface counter top installation
- Wooden lockers installed in Home team locker rooms
- Sports turf installed in weight room
- Duct sock installation in weight room completed
- Washer and Dryer installed in laundry room

### UPCOMING ACTIVITIES

- Begin weight room flooring installation
- Begin LVT installation
- Begin carpet installation
- Installation of mechanical screen wall area 2 roof

