


BCHS Renovation

WEEK OF Mar 8th, 2019

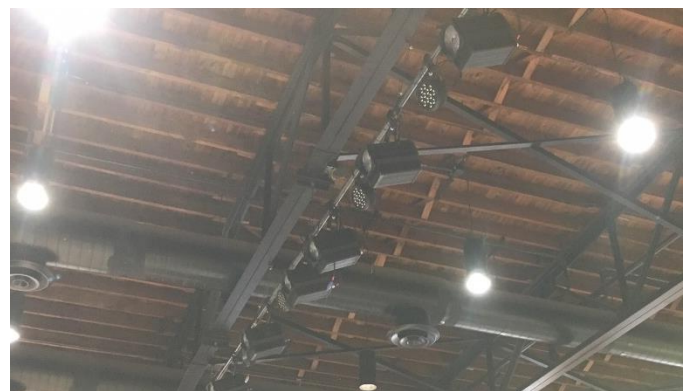

SAFETY

Safe Days Since Last Incident	207
Incidents to Date	0
First Aids to Date	2



WEATHER

Working Days	5
Days with Rain	2
Activities Delayed	0



SCHEDULE MILESTONES

- Stained and Sealed Auditorium Floor
- Hung new lights in Fitness and Wellness



MANPOWER

Number of Trades	7
Average Workers <i>(per day)</i>	24

TOP ACTIVITIES THIS WEEK

- Started installing ceiling grid on second floor of Auditorium
- Installed ceiling grid in Control Room and Lobby
- Installed main and branch sprinkler lines on 1st floor of North Wing
- Sanded and Painted Platform
- Installed acoustical panels in Auditorium
- Installed Ticket and Control Room window
- Installed base in Auditorium

UPCOMING ACTIVITIES

- Install lighting at casework in Backstage Area
- Install handrails at Auditorium
- Install LVT in Auditorium
- Install wheelchair lifts in Auditorium
- Install VCT in Green Room
- Continue installing ceiling grid on second floor of Auditorium
- Install trim in Auditorium

