


BCHS Renovation

WEEK OF Feb 22nd, 2019

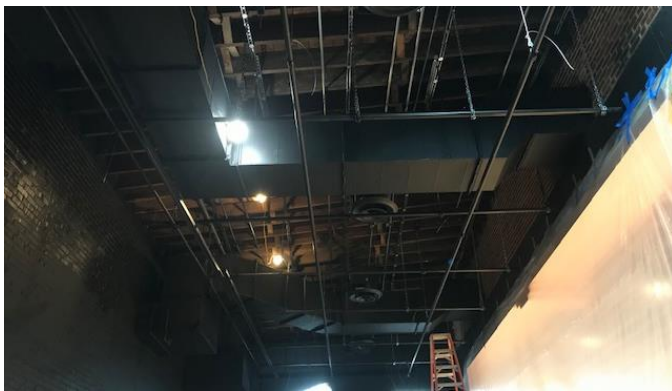

SAFETY

Safe Days Since Last Incident	197
Incidents to Date	0
First Aids to Date	2



WEATHER

Working Days	5
Days with Rain	3
Activities Delayed	0



SCHEDULE MILESTONES

- Finished installing Proscenium
- Installed Storefront at Auditorium



MANPOWER

Number of Trades	5
Average Workers <i>(per day)</i>	20

TOP ACTIVITIES THIS WEEK

- Started capping Science and Technology roof
- Installed main and branch sprinkler lines in Corridor A100.C
- Installed casework in Backstage Area
- Demoed ceiling on second floor of Auditorium
- Started electrical clean up above ceiling on second floor of Auditorium
- Demoed old lights in Fitness and Wellness

UPCOMING ACTIVITIES

- Install lighting at casework in Backstage Area
- Continue electrical clean up above ceiling on second floor of Auditorium
- Install new lights in Fitness and Wellness
- Stain Auditorium Floor
- Install VCT in Backstage Area
- Turn on units in Auditorium
- Install ceiling grid in Control Room and Lobby

