
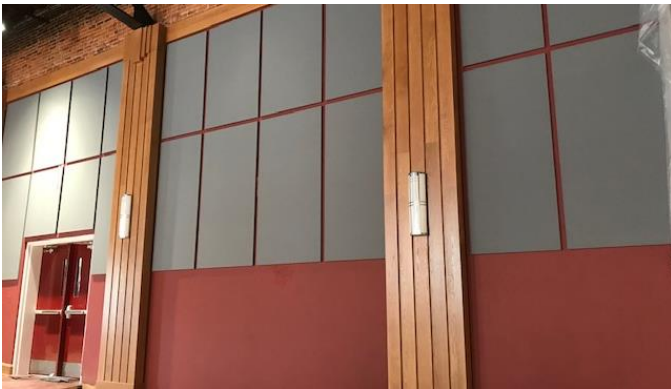


# BCHS Renovation

WEEK OF Mar 22nd, 2019



## SAFETY

Safe Days Since Last Incident 217

Incidents to Date 0

First Aids to Date 2



## WEATHER

Working Days 5

Days with Rain 0

Activities Delayed 0



## SCHEDULE MILESTONES

- Installed acoustical panels in Auditorium



## MANPOWER

Number of Trades 5

Average Workers (per day) 23

## TOP ACTIVITIES THIS WEEK

- Finished installing acoustical panels in Auditorium
- Installed roller shades in Auditorium
- Dropped ceiling tile on 2<sup>nd</sup> floor of Auditorium
- Installed tile under drinking fountains in Corridor A100.B
- Installed lights on platform
- Installed LVT in Auditorium and Lobby

## UPCOMING ACTIVITIES

- Install Auditorium seats
- Install VCT in Green Room
- Continue installing main and branch sprinkler
- Install performance lights on platform
- Install Platform curtains
- Landscaping at the front of the Auditorium

