


BCHS Renovation

WEEK OF Nov 23rd, 2018

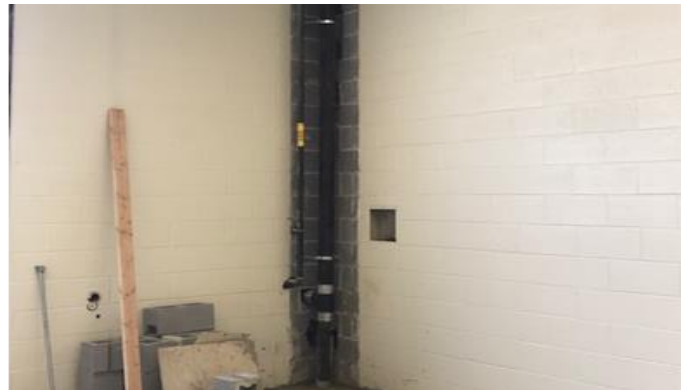

SAFETY

Safe Days Since Last Incident 131

Incidents to Date 0

First Aids to Date 2



WEATHER

Working Days 4

Days with Rain 0

Activities Delayed 0



SCHEDULE MILESTONES

- RTU's installed at Science and Technology



MANPOWER

Number of Trades 4

Average Workers (per day) 30

TOP ACTIVITIES THIS WEEK

- 3rd party Overhead Inspection
- Installed RTU's at Science and Technology
- Delivered Condenser Units for Auditorium
- Finished hanging drywall in Backstage Area
- Installed Flex and Grills at Grid Ceiling in Science and Technology
- Continued installing duct in backstage area
- Replaced roof drain in Project Studio

UPCOMING ACTIVITIES

- Finish sprinkler rough-in I2tech
- Hang duct in Project Studio
- Tile group toilet area
- Install duct at Stage/Mezzanine Area
- Install Sprinkler at Stage/Mezzanine Area
- Fire Alarm Wire pull in Auditorium

