


BCHS Renovation

WEEK OF Dec 28th, 2018

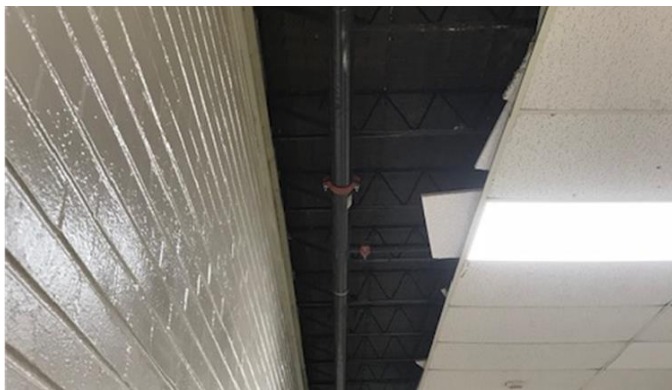

SAFETY

Safe Days Since Last Incident	158
Incidents to Date	0
First Aids to Date	2



WEATHER

Working Days	4
Days with Rain	1
Activities Delayed	0



SCHEDULE MILESTONES

- Completed sprinkler main and branch rough-in in Auditorium Crawspace



MANPOWER

Number of Trades	6
Average Workers <i>(per day)</i>	29

TOP ACTIVITIES THIS WEEK

- Started installing ceiling grid in Corridor A 100.A and A100.B
- Finished sprinkler main and branch rough-in in Auditorium Crawspace
- Saw Cut and Tied-In sewer line at Nurses Office
- Started main and branch rough-ins 2nd floor corridors of Auditorium Area
- Started electrical clean up above ceiling in Corridor A100.A and A100.B

UPCOMING ACTIVITIES

- Install ductwork at Stage/Mezzanine area
- Finish electrical clean up above ceiling in Corridor A100.A and A100.B
- Continue branch rough-ins 2nd floor corridors of Auditorium Area
- Slab infill at Nurses Area
- Continue installing duct at Nurses Area

