


Riverbank Elementary

WEEK OF June 11th, 2018

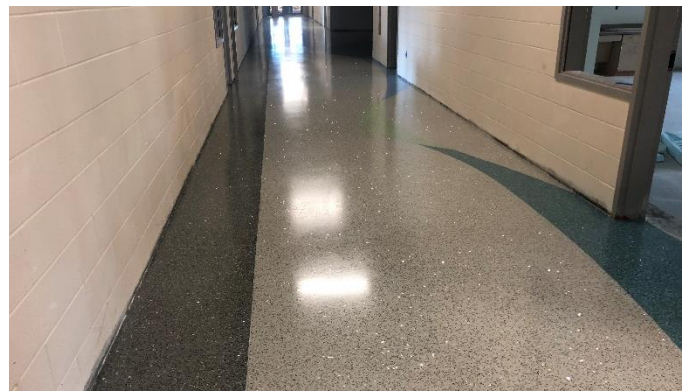

SAFETY

Incidents to Date	2
First Aids to Date	1



SCHEDULE

Current Completion August 1st 2018



WEATHER

Working Days	6
Days of Weather Delay	3
Activities Delayed	2



MANPOWER

Number of Trades	17
Average Workers <i>(per day)</i>	125

TOP ACTIVITIES THIS WEEK

- 1.9" of rain Monday delayed sitework and landscaping until site conditions dried out
- Maintaining Erosion Control
- Playground Equipment Installation
- Terrazzo Final Grid and Polish in Building A & D
- Pouring Main Lobby Terrazzo
- Curb/Stone Base at Drop Off Loop
- Toilet Partitions in Buildings A & B
- VCT Installation in Building A
- Brick columns at Canopies completed
- VRF Startup in Buildings A & D
- MEP Connections to Kitchen Equipment
- Irrigation Install ongoing

UPCOMING ACTIVITIES

- VRF Startup in Buildings B & C
- Landscaping at Emergency Access Road
- Solid Surface Installation
- Acoustic Wall Panels
- SCE&G Gas Line Installation
- Playground Turf Installation
- Elevator Inspection
- Area 5 3rd Party Overhead Inspection Wednesday
- OSF 2nd Floor Overhead Inspection Wednesday, June 27th

