
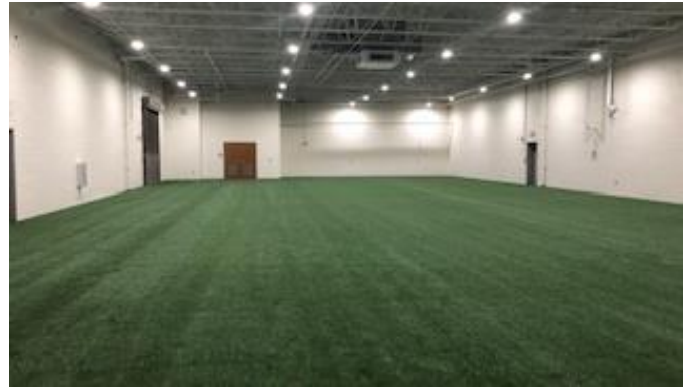


BCHS North Wing Renovation

WEEK OF July 20th, 2019



SAFETY

Safe Days Since Last Incident	39
Incidents to Date	0
First Aids to Date	0



WEATHER

Working Days	7
Days with Rain	0
Activities Delayed	0



SCHEDULE MILESTONES

- Installed turf in Fitness and Wellness
- Seal coated the road by Science and Technology building



MANPOWER

Number of Trades	5
Average Workers (per day)	23

TOP ACTIVITIES THIS WEEK

- Installed toilet fixtures in group toilet
- Seal coated road by Science and Technology Building
- Fixed the historic gate
- Installed ceiling grid in group toilet area
- Installed turf in Fitness and Wellness
- Started hanging markerboards in classrooms

UPCOMING ACTIVITIES

- OSF overhead inspection
- Drop ceiling tile in North Wing
- Finish installing markerboards and tackstrips
- Install toilet partition and accessories

