


# BCHS North Wing Renovation

WEEK OF June 21st, 2019

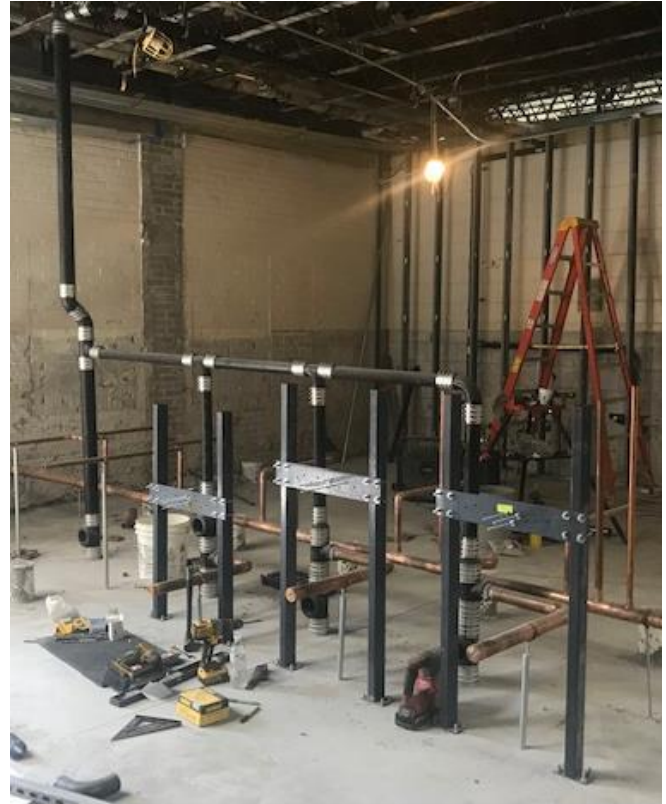

## SAFETY

Safe Days Since Last Incident	17
Incidents to Date	0
First Aids to Date	0



## WEATHER

Working Days	5
Days with Rain	1
Activities Delayed	0



## SCHEDULE MILESTONES

- Placed concrete slab in 1<sup>st</sup> floor Group Toilet



## MANPOWER

Number of Trades	5
Average Workers (per day)	33

### TOP ACTIVITIES THIS WEEK

- Placed concrete in 1<sup>st</sup> floor Group Toilets
- Finished installing ceiling grid in classrooms and corridor on 2<sup>nd</sup> floor
- Started installing new mechanical units on 1st floor
- Install door frames in 1st floor Group Toilet Area
- Started framing walls in 1<sup>st</sup> floor Group Toilet

### UPCOMING ACTIVITIES

- Overhead inspection for 2<sup>nd</sup> floor Classrooms and Corridor
- Install ceiling grid in 1<sup>st</sup> floor classrooms
- Continue above ceiling clean up in 1<sup>st</sup> floor classrooms
- Continue installing duct in Group Toilets

