
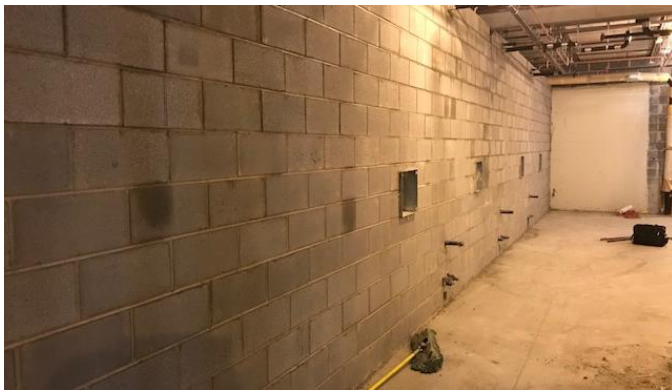


# BCHS Renovation

WEEK OF October 26th, 2018



**SAFETY**

Safe Days Since Last Incident	109
-------------------------------	-----

Incidents to Date	0
-------------------	---

First Aids to Date	1
--------------------	---

**WEATHER**

Working Days	5
--------------	---

Days with Rain	1
----------------	---

Activities Delayed	0
--------------------	---

**SCHEDULE MILESTONES**

31

Passed in-wall inspection at Project Studio

- Removed HVAC Unit on top of Fitness and Wellness building

**MANPOWER**

Number of Trades	7
------------------	---

Average Workers <i>(per day)</i>	33
-------------------------------------	----

## TOP ACTIVITIES THIS WEEK

- Demoed HVAC unit at Group Toilet area
- Removed HVAC unit above stage area
- Removed condensing unit from Auditorium area
- Completed CMU Wall between Room 402 and Group Toilets
- Completed in-wall electrical rough-in Project Studio
- Passed in-wall inspection at Project Studio
- Started hanging GWB in Project Studio
- Blockfill and prime Group Toilet walls

## UPCOMING ACTIVITIES

- Continue sprinkler rough in I2Tech
- Continue hanging GWB in Project Studio
- Install beams for doors at Backstage areas
- Hang duct in Auditorium
- Install sprinkler in Auditorium
- Inspect plumbing at backstage area
- Continue framing walls at backstage area
- Install RTU's at Project Studio

