


Saluda River Academy

WEEK OF August 3rd

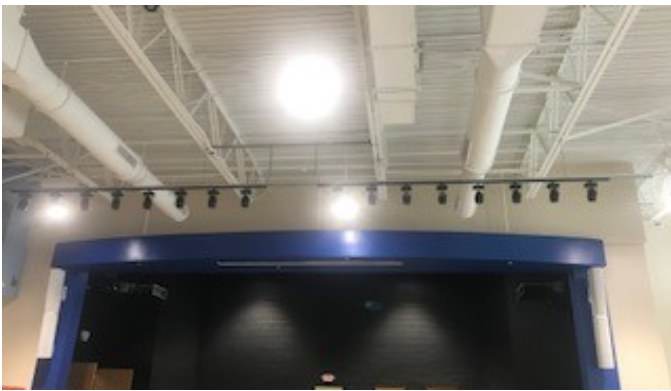

SAFETY

Safe Days Since Last Incident	127
Incidents to Date	1
First Aids to Date	0



WEATHER

Working Days	5
Days with Rain	3
Activities Delayed	0



SCHEDULE MILESTONES

DHEC kitchen reinspection 8/7/18



MANPOWER

Number of Trades	8
Average Workers <i>(per day)</i>	44

TOP ACTIVITIES THIS WEEK

- OSF punchlist
- DHEC kitchen inspection punchlist
- 3rd party chapter one punchlist
- Install radio repeater
- Install school furniture
- Install sound system area C
- Install stage track lighting
- Paint wood flooring at stage
- Install ornamental fencing
- Install chain link fence
- Sitework fine grading
- Install playground equipment

UPCOMING ACTIVITIES

- Install sports flooring area C
- Install stage curtain area C
- Install ADA lift at stage
- Install operable partition
- Install interior glass at doors
- Install serving line at kitchen
- Install trees
- Install sod
- DHEC kitchen reinspection

